Supplementary Material S2: Documented Programs Read Through KMC

Supplement to: P. K. de Albuquerque, D. R. Pleffken, C. S. Cerqueira, and L. Galembeck, "Knowledge–Maturity Coevolution: A Coupled Evidence Model for Selecting Simulation and Test Activities in Constrained Engineering Development," IEEE Access.

This supplement expands Section VI-C of the article. Numbers in brackets refer to the article's reference list; the cited items are reproduced at the end. Section, table, and equation numbers without the prefix S2 refer to the article. All sources are public. The readings are retrospective and were made with the outcomes known; they illustrate whether the mechanisms of the model appear in documented decisions and do not calibrate the model or show that KMC would have changed any decision.

1. Selection and coding

Six aerospace programs with public, primary or near-primary documentation of the sequence of analyses, tests, discrepancies, and corrective actions were selected purposively: the Hyper-X Launch Vehicle (HXLV) of the X-43A program, the Saturn V all-up test decision, the F-1 combustion-instability program, Falcon 1, and the X-51A and DARPA Hypersonic Technology Vehicle 2 (HTV-2) programs. The selection is illustrative, not a representative sample of development programs.

For each program, documented events were coded by activity class (S: analysis and simulation; E: separate-effects or component testing; T: integrated ground or flight testing), by whether a test produced an epistemic shock (a negative reassessment after evidence undermined a prior claim, Section III-B), and by the evidence available before the next integrated test. No numerical K or M was assigned, because the public record does not contain criterion-level evidence for complete profiles (see 2.2 below). Where the record names a specific deficiency, it is mapped to the criteria of the operational rubric (Table 4): for K, causal coverage, mechanistic depth, coherence, uncertainty understanding, and domain definition; for M, demonstrated performance, representativeness, integration fidelity, decision robustness, and control and repeatability.

2. X-43A Hyper-X Launch Vehicle (HXLV)

2.1 Claims and documentary corpus

The case concerns the HXLV booster, not the X-43A research vehicle (HXRV); findings on one are not transferred to the other. Three claims were defined: C1, the aerodynamic and actuator models used for stability assessment; C2, the uncertainty procedure for the intended trajectory; and C3, boost control capability. C1 and C2 concern models and procedures, C3 the vehicle, and their maturity is not aggregated.

The bounded corpus comprises eight public documents dated 2000–2025: the preflight program paper [54], the mishap investigation [14], the return-to-flight review [55], two NASA releases on the second flight [56], [57], the flight-2 guidance and control paper [58], the 2004 research engineering report [59], and the NASA historical page [60]. From them, 19 parent records yield 20 observations, one of which (a conflicting release altitude) is retained only for discrepancy auditing. A 2004 incident release [61] and a lessons-learned review [62] were added later as a separately logged extension and did not change the original records.

Records were grouped in four cumulative documentary epochs: E1, preflight planning (October 2000); E2, investigation (through May 2003); E3, corrective actions (through March 2004); and E4, retrospective results (through June 2006). The epochs contain 3, 7, 14, and 19 observations. Publication dates delimit the epochs; they do not establish what individual engineers knew, and later reconstructions were excluded from earlier epochs. Repeated accounts of the same event were linked rather than counted as independent demonstrations. Conflicting values were preserved rather than averaged: the first-flight release altitude appears as about 20,000 ft [55], 24,000 ft [56], and 23,000 ft [60], and the 22,244 ft reported at failure time 13.5 s [14] is not a release altitude.

2.2 Coverage audit

The audit enumerates 120 units: three claims × ten rubric criteria × four epochs. For each unit it recorded the candidate passages, the configuration to which they apply, the missing information, and whether the evidence was sufficient for a complete anchored assessment. None was: every unit remained not assessed. Typical gaps were final model versions and complete parameter distributions (C1, C2), closure of reviews and acceptance records, repeatability, and activity-level costs (C3), and export-controlled material omitted from the public investigation [14]. The result supports the restriction of the article to qualitative readings; it does not show that the program lacked the evidence.

2.3 Sequence

The preflight paper reported control-law refinement and Monte Carlo analysis of aerodynamic and flight-control uncertainties, and a trajectory different from that of the heritage booster [54]. After the loss of control during boost on 2 June 2001, the investigation found inaccuracies in inherited and HXLV-specific models: corrected nominal models reduced the predicted roll-axis gain margin from 8 dB to less than 2 dB against a 6 dB requirement, and reproducing the mishap required combining the model corrections with parameter uncertainty [14] (Fig. S2-1). Return to flight combined wind-tunnel and actuator tests, revised models, comparisons of independent boost simulations, stronger actuators, and propellant off-loading for a higher-altitude release that reduced exposure [55], [56]. A test-setup anomaly on 11 February 2004 exceeded the qualified actuator torque and led to replacement and investigation before the second flight [61]. On 27 March 2004 the HXLV delivered the research vehicle at 28.67 km (94,069 ft) against 28.63 km (93,932 ft) planned and at Mach 6.946 against 7.075 [57], [58], and the Mach 10 flight later in 2004 also achieved separation within tolerances [59]. A lessons-learned review relates the accident to heritage assumptions, representative testing, stability margins, and uncertainty and dynamic modeling [62]. Fig. S2-2 separates the event dates from the dates of the documents that report them.

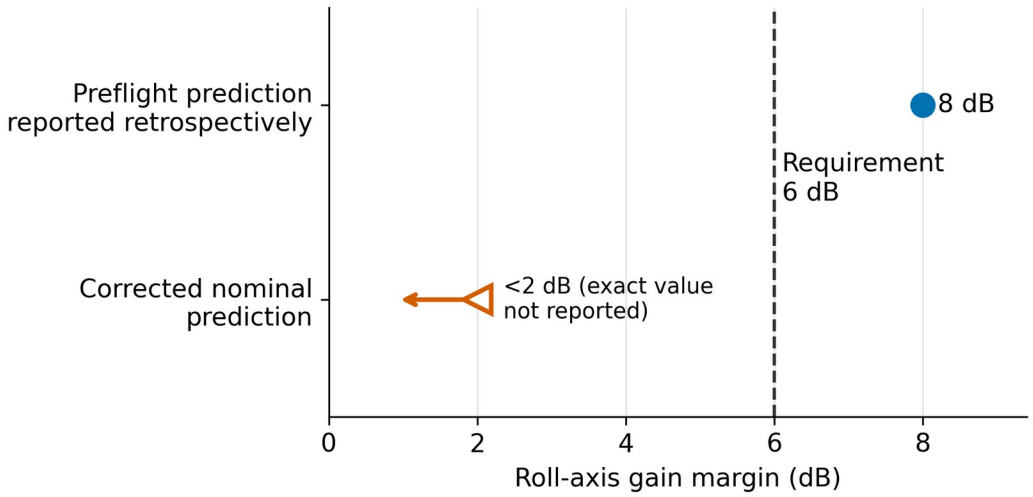


Fig. S2-1. Reported X-43A roll-axis gain margin before and after nominal model correction [14, pp. 6–7]. The corrected value is reported only as less than 2 dB (open marker: upper bound); the requirement is 6 dB. These are model predictions, not flight measurements or KMC scores.

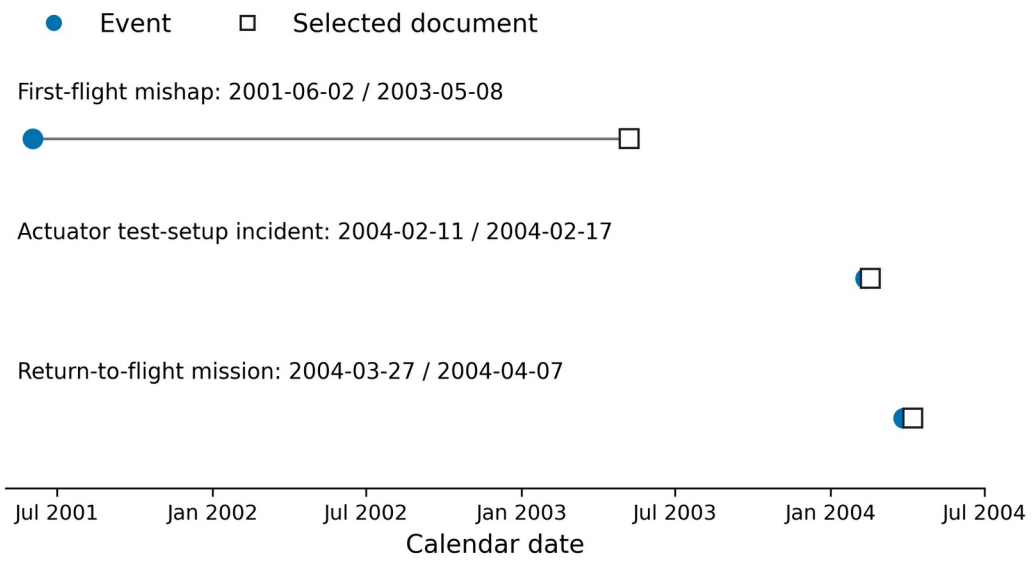


Fig. S2-2. Event dates and dates of selected documents for the first-flight mishap [14], the actuator incident [61], and the return-to-flight mission [57]. Connecting segments associate an event with a record; their lengths do not measure decision delay.

2.4 Reading through the model

In the terms of the article, an integrated test was attempted while knowledge of the configuration-specific claims rested on heritage transfer, and the result was an epistemic shock on C1–C3. Recovery came from the activities the model favors after a shock: separate-effects testing, revised models, and joint-uncertainty simulation, together with reduced exposure. Table S2-1 links the main observations to rubric criteria. Table S2-2 lists the postflight findings examined in the extension, and Table S2-3 a time-bounded check that uses only documents available before each flight, with cutoffs at the end of 1 June 2001 and 26 March 2004. The preflight sources support requests for evidence about domain transfer and uncertainty adequacy, but they do not establish that the model error was detectable before flight: the program, not KMC, detected and corrected the problems, and an equally informed conventional review could reach the same questions.

Table S2-1. X-43A observations and KMC reasoning (retrospective).

Observation	Claim and rubric criteria	Implied action	Inference excluded
Corrected roll margin below requirement [14]	C1 domain definition, coherence; C2 uncertainty understanding	Reconcile model and uncertainty bounds before renewed acceptance	No numerical drop in K or M; no claim of earlier prediction
Nominal corrections alone did not reproduce the mishap [14]	C2 decision robustness	Require justified joint variations before closing the gate	Uncertainty analysis already existed [54]
Stronger actuators and modified trajectory [55], [56]	C3 representativeness	Declare the new baseline; verify changed interfaces and envelope	No automatic recovery from completing a corrective action
Actuator torque exceedance before flight 2 [61]	C3 demonstrated performance	Keep acceptance open until the replacement is verified	Program detected it without KMC
Flight-2 delivery within tolerance [57], [58]	C3 demonstrated performance	Credit the delivery point, not full-envelope repeatability	No transfer of HXRV results or of the Mach 10 flight as a Mach 7 repetition

Table S2-2. Postflight findings and KMC reasoning (extension PF01–PF05).

Entry and evidence	Rubric criteria	Candidate response	Inference limit
PF01: inherited and HXLV-specific model deficiencies; corrected roll margin below requirement [14, pp. 6–7], [62]	C1 domain definition, coherence; C3 representativeness	Reopen model acceptance; require configuration-specific corroboration	Post-mishap diagnosis; no demonstrated preflight signal
PF02: corrected nominal	C2 uncertainty understanding,	Require justified joint	Uncertainty analysis already

models alone did not reproduce the mishap; combined uncertainty was required [14, pp. 6–7]	decision robustness	variations before closing the gate	existed [54]; KMC does not discover omitted physics
PF03: return-to-flight actions revised models, actuators, and launch conditions [55]	C1–C3 separately: domain definition, representativeness	Rebaseline affected claims; verify the changed configuration	A design correction does not itself demonstrate recovered maturity
PF04: 11 February 2004 test-setup anomaly exceeded qualified torque; replacement and investigation required [61]	C3 demonstrated performance, representativeness	Keep actuator acceptance open pending disposition and verification	Program detected the anomaly without KMC
PF05: flight-2 HXLV separation results and HXRV response discrepancies concern distinct objects [58]	C3 demonstrated performance	Accept only the supported delivery-point claim; keep out-of-scope discrepancies separate	Success is not full-envelope repeatability; HXRV discrepancies cannot lower HXLV assessments

Table S2-3. Time-bounded documentary check before flights 1 and 2. G: evidence request; R: review trigger already recognized by the program; U: no eligible preflight indication.

ID / code	Preflight record or exclusion	KMC review implication	What is established
PR01 / G	Flight 1: trajectory different from the heritage booster [54, pp. 2–3]	Request evidence for transferring heritage models	Domain difference known; specific error not established
PR02 / G	Flight 1: uncertainty analysis already reported [54, p. 3]	Review bounds and combinations for the intended claim	Existing analysis; inadequacy not established
PR03 / G	Flight 1: tests planned in the 2000 account [54, p. 5]	Request dated completion and disposition records	No evidence that tests remained unfinished at launch
PR04 / U	Flight 1: corrected margin comes from the 2003 report [14, pp. 6–7]	Exclude hindsight from preflight diagnosis	No eligible preflight indication
PR05 / R	Flight 2: actuator qualification exceeded [61, paras. 1–2]	Require replacement and verification before closing acceptance	Program already detected and investigated
PR06 / R	Flight 2: autopilot retuning considered [61, para. 3]	Link revised parameters to verification evidence	Program already recognized the review need
PR07 / R	Flight 2: corrective models, hardware, and simulations [55, pp. 4–7]	Trace the changed configuration to evidence for each claim	Corrective work already documented; no new defect inferred

2.5 From evidence to the next activity

Two chains connect a documented observation to the choice of the next evidence-producing activity (Table S2-4). Chain A uses the investigation [14, pp. 6–7]: corrected nominal models remain stable and do not reproduce the loss of control, so coherence (C1) and uncertainty adequacy (C2) remain open, and the retained sequence couples targeted tests with joint-uncertainty simulation rather than closing on nominal stability. Chain B uses only the release of 17 February 2004 [61], before flight 2: exceeding the qualified torque removes the basis for accepting that actuator, so the retained sequence replaces and verifies it. One criterion can be coded from the record: for flight-1 boost control (C3), demonstrated performance is at level 0, because the essential performance criteria failed. The other nine criteria, and a comparable preflight profile, are not assessed, so no (K, M) point or slope dM/dK can be computed; the criterion-based branch of the procedure remains usable where the derivative-based branch is not. In both chains the program reached the same actions without KMC; the alternatives are analytical comparisons, not a recovered historical trade study, and their costs and durations are unknown.

Table S2-4. Candidate activities after the two documented observations. "Retained" denotes a plan for obtaining evidence; acceptance remains open until its completion criteria are verified.

ID	Candidate activity	Criterion-based disposition	Evidence needed before closure
A1	Correct nominal models only	Insufficient: does not reconcile the observed instability	Explanation of the residual discrepancy
A2	Joint-uncertainty simulation alone	Useful but conditional: unsupported bounds cannot	Traceable bounds, model versions, and discriminating

		establish adequacy	comparisons
A3	Targeted tests plus coupled model and uncertainty analysis	Retained	Measured support for key dynamics; traceable joint variations; applicability limits
B1	Keep the affected actuator because it may still function	Excluded by the documented replacement requirement [61]	Functioning alone does not dispose of the exceedance
B2	Retune the autopilot or simulate without replacing the unit	Insufficient for the hardware qualification condition	Disposition of the installed hardware
B3	Replace and verify the actuator; coordinate retuning and investigation	Retained, consistent with the announced parallel activities [61]	Replacement identity, acceptance results, and integrated control verification

3. Saturn V all-up testing

On 31 October 1963, Mueller directed that the first Saturn IB and Saturn V flights use all live stages and complete spacecraft, and that mission planning assume two successful flights before a crewed flight [63]. The first Saturn V flight, Apollo 4 on 9 November 1967, succeeded [17]. Apollo 6, on 4 April 1968, experienced pogo oscillations, the early shutdown of two second-stage engines, and a failed third-stage restart [17]. Engineers detuned the F-1 engines, charged the liquid-oxygen prevalve cavities with helium, and redesigned the J-2 augmented spark igniter lines, and on 27 April 1968 the third Saturn V was approved for a crew [17]. In the terms of the article, all-up testing concentrated maturity evidence in few expensive integrated tests; Apollo 6 produced shocks from couplings visible only at integrated level, and the program restored headroom through diagnosis and ground-verified fixes before the next integrated test, as steps 4 and 5 of Table 6 would direct.

4. F-1 combustion instability

Between October 1962 and September 1966, Project First, the F-1 combustion-stability program, conducted about 2000 of the roughly 3200 full-scale F-1 tests, combining fourteen injection patterns with fifteen baffle configurations and rating stability with bombs producing perturbations of about 100% of chamber pressure; full-scale test data were described as the most reliable source of design information [15]. The flight injector accumulated 703 engine tests [15]. This is the weak-simulation regime of Section V-C: with a low data-limited ceiling $\bar{K}$, the model prescribes discriminating physical tests rather than more analysis, and the bomb test is a separate-effects stimulus that makes stability observable. The cost of the regime, thousands of full-scale tests, illustrates why weak simulation penalizes analysis-first and test-first logics in the model.

5. Falcon 1

Falcon 1 failed on its first three flights, in March 2006 (fuel leak and fire), March 2007 (second-stage control lost to propellant slosh), and August 2008 (first stage recontacted the second stage after separation), and reached orbit on 28 September 2008 [16], [64]. Each failure revealed a different mode and was followed by diagnosis and correction. Flights cost about 8 million US dollars against roughly 100 million for development [16]. In the terms of the article this is test-first development with integrated tests that were affordable relative to the program: shocks are frequent when knowledge is low, and the program reached the target after three of them. The record does not show how much each flight taught, and whether ground tests could have exposed these modes at lower cost is not established; Section VI-B of the article discusses why the launch-vehicle estimates support strong learning in flight only conditionally.

6. X-51A and HTV-2

The X-51A scramjet demonstrator flew four times. In May 2010 it flew for more than three minutes at Mach 4.88 under scramjet power [65]; in June 2011 the inlet unstarted during the transition to JP-7 fuel and restart attempts failed [66]; in August 2012 a cruiser control-fin fault caused the loss of the vehicle before scramjet ignition [65]; and on 1 May 2013 it flew for more than six minutes, three and a half under scramjet power, at Mach 5.1 [67]. The DARPA HTV-2 glider was lost on both of its flights. After the April 2010 flight, the

engineering review board found higher-than-predicted adverse yaw coupled into roll that exceeded the available roll control [68]. That aerodynamic knowledge was incorporated into the August 2011 flight, which achieved controlled Mach 20 flight before unexpected aeroshell degradation caused upsets of increasing severity [68], [69]. The program manager stated that extrapolating from known flight regimes and relying solely on advanced thermal modeling and ground testing could not predict the Mach 20 environment [69].

In the terms of the article, this is the data-limited ceiling $\bar{K}$ stated by the programs themselves: analysis and ground testing could not raise configuration-specific knowledge to K_{need}, so each flight was both a demonstration and the main source of new knowledge, and each loss was an epistemic shock that exposed a different claim (propulsion, control surfaces, aerodynamic coupling, thermal protection).

7. Cross-case reading

Table S2-5 (Table 9 of the article) summarizes the six cases. In the five flight programs, integrated tests that exposed configuration-specific or integrated-level knowledge gaps produced shocks (X-43A flight 1, Apollo 6, Falcon 1 flights 1–3, X-51A flights 2–3, both HTV-2 flights), and success followed separate-effects testing, diagnosis, or analysis that restored headroom; in the F-1 program, the absence of predictive capability led directly to discriminating physical tests. The cases span the scenarios of Section V-C: costly, high-consequence integrated tests (X-43A, Saturn V), weak simulation (F-1, HTV-2, X-51A), and affordable flights (Falcon 1).

Table S2-5. Documented sequences read through the model (Table 9 of the article).

Program	Documented sequence	KMC reading	Model regime
X-43A (2001–2004)	Flight 1 lost; models, wind-tunnel and actuator tests revised; flights 2–3 successful [14], [55]–[59]	T without headroom → shock; E and S restore headroom → T succeeds	Costly, risky tests
Saturn V (1963–1968)	All-up decision; Apollo 4 success; Apollo 6 pogo and J-2 failures; fixes; crewed Apollo 8 [17], [63]	Few integrated tests; integrated-level shock; diagnosis before next T	Costly, high-consequence tests
F-1 engine (1962–1966)	About 2000 full-scale tests with bomb rating; 703 tests of flight injector [15]	Low data-limited ceiling; discriminating physical tests replace analysis	Weak simulation
Falcon 1 (2006–2008)	Three failures with distinct modes; success on flight 4 [16], [64]	Test-first at low K; each shock adds knowledge	Cheap tests relative to program
X-51A (2010–2013)	Partial success; inlet unstart; fin fault; success on flight 4 [65]–[67]	Each flight both demonstration and main knowledge source; shocks on different claims	Costly tests, low data-limited ceiling
HTV-2 (2010–2011)	Two losses: yaw–roll coupling, then aeroshell degradation [68], [69]	Ground testing and modeling could not reach K_{need}; flight-only learning	Costly, high-consequence tests; weak simulation

8. Limitations

The cases were selected purposively and read with the outcomes known; the coding was not blinded or preregistered. Public documents omit export-controlled material, contemporary decision records, and activity-level costs, so no numerical K or M, no cost of alternatives, and no earlier detection or avoided loss can be established. The readings show that the mechanisms of the model are visible in documented decisions; they do not calibrate the model, test its coefficients, or show that KMC would have produced better decisions than the reviews the programs carried out.

References (numbering of the article)

[14] X-43A Mishap Investigation Board, "Report of findings: X-43A mishap, vol. I," NASA, Washington, DC, USA, May 8, 2003. Accessed: Oct. 6, 2026. [Online]. Available: https://www.nasa.gov/wp-content/uploads/2015/01/47414main_x43A_mishap.pdf

[15] J. C. Oefelein and V. Yang, "Comprehensive review of liquid-propellant combustion instabilities in F-1 engines," J. Propuls. Power, vol. 9, no. 5, pp. 657–677, Sep. 1993, doi: 10.2514/3.23674.

[16] T. Malik, "SpaceX successfully launches Falcon 1 rocket into orbit," Space.com, Sep. 29, 2008. Accessed: Oct. 6, 2026. [Online]. Available: https://www.space.com/5905-spacex-successfully-launches-falcon-1-rocket-orbit.html

[17] J. Uri, "55 years ago: NASA administrator Webb OKs flying a crew on the third Saturn V," NASA History, Apr. 27, 2023. Accessed: Oct. 6, 2026. [Online]. Available: https://www.nasa.gov/history/55-years-ago-nasa-administrator-webb-oks-flying-a-crew-on-the-third-saturn-v/

[54] V. L. Rausch, C. R. McClinton, J. Sitz, and P. Reukauf, "NASA's Hyper-X program," presented at the 51st Int. Astronaut. Congr., Rio de Janeiro, Brazil, Oct. 2–6, 2000, Paper IAF-00-V.4.01. Accessed: Oct. 6, 2026. [Online]. Available: https://ntrs.nasa.gov/citations/20010075170

[55] D. E. Reubush, L. T. Nguyen, and V. L. Rausch, "Review of X-43A return to flight activities and current status," presented at the 12th AIAA Int. Space Planes Hypersonic Syst. Technol. Conf., Norfolk, VA, USA, Dec. 2003, AIAA Paper 2003-7085. Accessed: Oct. 6, 2026. [Online]. Available: https://ntrs.nasa.gov/citations/20040040296

[56] NASA Dryden Flight Research Center, "NASA's X-43A hypersonic aircraft ready for flight," Edwards, CA, USA, Release 04-14, Mar. 24, 2004. Accessed: Oct. 6, 2026. [Online]. Available: https://www.nasa.gov/news-release/nasa-dryden-flight-research-center-news-room-news-releases-nasas-x-43a-hypersonic-aircraft-ready-for-flight/

[57] NASA Dryden Flight Research Center, "NASA's X-43A flight results in treasure trove of data," Edwards, CA, USA, Release 04-20, Apr. 7, 2004. Accessed: Oct. 6, 2026. [Online]. Available: https://www.nasa.gov/news-release/nasa-dryden-flight-research-center-news-room-news-releases-nasas-x-43a-flight-results-in-treasure-trove-of-data/

[58] C. Bahm, E. Baumann, J. Martin, D. Bose, R. E. Beck, and B. Strovers, "The X-43A Hyper-X Mach 7 flight 2 guidance, navigation, and control overview and flight test results," presented at the AIAA/CIRA 13th Int. Space Planes Hypersonic Syst. Technol. Conf., Capua, Italy, May 2005. Accessed: Oct. 6, 2026. [Online]. Available: https://ntrs.nasa.gov/citations/20050182778

[59] L. Grindle and C. Bahm, "The X-43A (Hyper-X) flies into the record books," in 2004 Research Engineering Annual Report, NASA Dryden Flight Research Center, Edwards, CA, USA, Jun. 2006. Accessed: Oct. 6, 2026. [Online]. Available: https://ntrs.nasa.gov/citations/20060056098

[60] NASA, "X-43A Hyper-X," last updated Aug. 15, 2025. Accessed: Oct. 6, 2026. [Online]. Available: https://www.nasa.gov/reference/x-43a/

[61] NASA Dryden Flight Research Center, "X-43A flight delayed," Edwards, CA, USA, Release 04-06, Feb. 17, 2004. Accessed: Oct. 6, 2026. [Online]. Available: https://www.nasa.gov/news-release/nasa-dryden-flight-research-center-news-room-news-releases-x-43a-flight-delayed/

[62] C. N. Dennehy, "GN&C lessons learned and associated best practices," presented at ESA/ESTEC, Noordwijk, The Netherlands, Jun. 6, 2017. Accessed: Oct. 6, 2026. [Online]. Available: https://ntrs.nasa.gov/citations/20200009546

[63] G. E. Mueller, "Revised manned space flight schedule," NASA memorandum M-C M 9330.186, Oct. 31, 1963. Accessed: Oct. 6, 2026. [Online]. Available: https://www.american-spacecraft.org/documents/sp-4503/document-7.html

[64] S. Clark, "Falcon 1 suffers another setback," Spaceflight Now, Aug. 3, 2008. Accessed: Oct. 6, 2026. [Online]. Available: https://spaceflightnow.com/falcon/003/failure.html

[65] Air Force Research Laboratory, "X-51A flight ends prematurely," Wright-Patterson AFB, OH, USA, Aug. 15, 2012. Accessed: Oct. 6, 2026. [Online]. Available: https://www.edwards.af.mil/News/AFMC-News/Article/153597/x-51a-flight-ends-prematurely/

[66] 95th Air Base Wing Public Affairs, "Second hypersonic flight ends prematurely, brings new flight test data," U.S. Air Force, Jun. 15, 2011. Accessed: Oct. 6, 2026. [Online]. Available: https://www.af.mil/News/Article-Display/Article/113041/second-hypersonic-flight-ends-prematurely-brings-new-flight-test-data/

[67] Boeing, "Boeing X-51A WaveRider sets record with successful 4th flight," news release, May 3, 2013. Accessed: Oct. 6, 2026. [Online]. Available: https://boeing.mediaroom.com/2013-05-03-Boeing-X-51A-WaveRider-Sets-Record-with-Successful-4th-Flight

[68] Defense Advanced Research Projects Agency, "14-F-0122 DARPA X-51 documents," FOIA release, Washington Headquarters Services FOIA Reading Room, 2014. Accessed: Oct. 6, 2026. [Online]. Available: https://www.esd.whs.mil/Portals/54/Documents/FOID/Reading%20Room/DARPA/14-F-0122_DARPA_X-51_DOCUMENTS.pdf

[69] Defense Advanced Research Projects Agency, "DARPA HTV-2 second test flight report released," SpaceRef, Apr. 20, 2012. Accessed: Oct. 6, 2026. [Online]. Available: https://spaceref.com/newspace-and-tech/darpa-htv-2-second-test-flight-report-released/
